

Ship 07-14

Work Order ID 164046

164046

Page 1

Wednesday, July 12, 2017 11:30:43 AM

Item ID: D4634-145 Accept *N900040100* Setup Start *NS1*
 Revision ID: Stop *NS2*
 Item Name: Aft, Center Ceiling Replacement Panel Assembly

Start Date: 7/13/2017 Start Qty: 3.00 *3*
 Required Date: 7/14/2017 Req'd Qty: 3.00 *3*
 Cust Item ID:
 Customer:

Reference:

Approvals: Process Plan:  Date: JUL 12 2017 Tooling: Date: Run Start *NR1*
 QC: Date: SPC (Y/N): Date: Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D4634	G

100	0.00								
100									
HandThermo	Memo	2.49							
Hand Finishing Thermoforming	Pick Kit								

110	0.00								
110									
Small Fab	Memo	3.93							
Small Fab	Assemble as per Dwg D4634-145								

1- Scuff bonding surface to eliminate in-perfections and increase bonding and clean with wash& wipe

2- Locate and glue down Channel Assy, angles, brackets, and mounting pads using 3M Plastic welder II.

Batch # M 137629

Expiry Date Sept 27/17.

3- Apply labels as per Dwg. and seal with 3M 3950 edge sealer

JUL 17 2017

D/ 6 9-8

DAS 07 9-89

17/07/18

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : _____					

Work Order ID 164046

Wednesday, July 12, 2017 11:30:43 AM

164046

Page 2

Item ID: D4634-145 Accept *N900040100* Setup Start *NS1*
 Revision ID: Stop *NS2*
 Item Name: Aft, Center Ceiling Replacement Panel Assembly
 Start Date: 7/13/2017 Start Qty: 3.00 *3* Cust Item ID:
 Required Date: 7/14/2017 Req'd Qty: 3.00 *3* Customer:
 Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start *NR1*
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
125	QC5- Inspect part completeness to step on W/O	0.00							UAS 38 9-89
125									
QC	Memo	0.06							111 18 2017
Quality Control									
130	Identify as per dwg & Stock Location: _____	0.00							
130									
Packaging	Memo	0.03							DAS 27 9-89 JUL 18 2017
Packaging	Sold								
140	QC21- Final Inspection - Work Order Release	0.00							
140									
QC	Memo	0.30							DAS 21 9-89 JUL 18 2017
Quality Control									
									DAS 21 9-89 JUL 18 2017

DQA: _____ Date: _____

**WORK ORDER NON-CONFORMANCE / UPDATE**

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS <table style="width:100%; border: none;"> <tr> <td style="border: none;">Skid-tube ☐</td> <td style="border: none;">Cross tube ☐</td> <td style="border: none;">Water Jet ☐</td> <td style="border: none;">Engineering ☐</td> </tr> <tr> <td style="border: none;">Machining ☐</td> <td style="border: none;">Small Fab ☐</td> <td style="border: none;">Prod. Eng. Coord. ☐</td> <td style="border: none;">Quality ☐</td> </tr> <tr> <td style="border: none;">Thermoforming ☐</td> <td style="border: none;">Finishing ☐</td> <td style="border: none;">Rec/Store/Packaging ☐</td> <td style="border: none;">Other ☐</td> </tr> <tr> <td style="border: none;">Large Fab ☐</td> <td style="border: none;">Composite ☐</td> <td style="border: none;">Supplier ☐</td> <td></td> </tr> </table>						Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐	
Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐																						
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐																						
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐																						
Large Fab ☐	Composite ☐	Supplier ☐																							
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval																		
Description Work Order Deviation				Disposition			Completed By																		
							Lead hand / Supervisor Approval Verification																		
							QC / QA Coordinator Approval																		
Root Cause		FAULT CATEGORY																							
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐	OTHER : ☐																			

Picklist Print

Wednesday, July 12, 2017 11:31:02 AM

Page 1

Work Order ID: 164046

164046

Parent Item: D4634-145

D4634-145

Parent Item Name: Aft, Center Ceiling Replacement Panel Assembly

Start Date: 7/13/2017

Required Date: 7/14/2017

Start Qty: 3.00

Required Qty: 3.00

Comments: IPP Rev. A 12/08/09 New Issue DL
 12/11/08 Document release DL VERIFIED BY:JLM IPP Rev B
 Dwg Update DL verf: DD IPP Rev C 13/07/09
 DL IPP Rev D Dwg Update 13/12/23
 DL IPP REV E Dwg update 14/01/09
 DL IPP Rev F Dwg. update 14/02/03
 DL IPP Rev G Dwg. Update 15/01/27 DL

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
D4636-5 *D4636-5* Bracket		Manufactured	No			100	Each	22.0000	1	✓			
									**				
					<u>Location</u>			<u>Loc Qty</u>		<u>Loc Code</u>			
					ST115			22					
					154916			22					
D4712-1 *D4712-1* Bracket		Manufactured	No			100	Each	3.0000	1	✓			
									**				
					<u>Location</u>			<u>Loc Qty</u>		<u>Loc Code</u>			
					MF004			3					
					149103			3					
D5021-5 *D5021-5* Foam, Center Panel, Aft		Manufactured	No			100	Each	1.0000	1	✓			
									**				
					<u>Location</u>			<u>Loc Qty</u>		<u>Loc Code</u>			
					ST479a			1					
					158843			1					

JUL 18 2017

DAS
6
9-89

JUL 18 2017

DAS
6
9-89

JUL 18 2017

DAS
6
9-89

~~164046X2~~

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐																																																													
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval																																																										
Description Work Order Deviation				Disposition				Completed By																																																									
021714								Lead hand / Supervisor Approval Verification																																																									
								QC / QA Coordinator Approval																																																									
Root Cause		FAULT CATEGORY																																																															
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐	Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐	Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐	Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐	Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐	Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐	Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐	Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐	LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐	Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐	Past Expiry Date ☐	Manufacturing Process ☐	OTHER : ☐			
Misidentified ☐	Past Due ☐																																																																

Picklist Print

Wednesday, July 12, 2017 11:31:02 AM

Page 2

Work Order ID: 164046

164046

Parent Item: D4634-145

D4634-145

Parent Item Name: Aft, Center Ceiling Replacement Panel Assembly

Start Date: 7/13/2017

Required Date: 7/14/2017

Start Qty: 3.00

Required Qty: 3.00

MS20426AD3-4

Purchased

No

100

Each

7,458.000

4

12

DAS
6
9-89

MS20426AD3-4

RIVET

**

Location

Loc Qty

Loc Code

GA

5872

m134294

1921

m136444

3951

ST312

1586

~~m134294~~

1586

124
6

MS20426AD4-6

Purchased

No

100

Each

1,714.000

2

6

DAS
6
9-89

MS20426AD4-6

Rivet

**

Location

Loc Qty

Loc Code

CCK004

979

M137851

979

GA

539

M134502

25

M137851

514

ST311

196

M136537

196

25
6

MS21059L08

Purchased

No

100

Each

121.0000

2

6

DAS
6
9-89

MS21059L08

Nut

**

Location

Loc Qty

Loc Code

ST300

121

m134943

21

m136554

100

B

D4634-5

Manufactured

No

100

Each

0.0000

1

3

DAS
07
9-89

D4634-5

Aft, Center Ceiling Panel

B163144 (X)

**

(X)

17/07/17

Wednesday, July 12, 2017 11:31:02 AM

Shop Packet Print

Page 2

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QS1042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : _____					

Picklist Print

Wednesday, July 12, 2017 11:31:02 AM

Work Order ID: 164046

164046

Parent Item: D4634-145

D4634-145

Parent Item Name: Aft, Center Ceiling Replacement Panel Assembly

Start Date: 7/13/2017

Required Date: 7/14/2017

Start Qty: 3.00

Required Qty: 3.00

D4647-1 Manufactured No

100 Each 7.0000 1

D4647-1

Doubler

**

DAS

6

9-89

Location

Loc Qty

Loc Code

MF004

6

155884

6

ST116

1

154781

1

D4664-5 Manufactured No

100 Each 39.0000 6

D4664-5

Spacer

**

DAS

6

9-89

Location

Loc Qty

Loc Code

MF004

39

154825

9

155824

30

D4732-17 Manufactured No

100 Each 5.0000 1

D4732-17

Label

**

DAS

6

9-89

Location

Loc Qty

Loc Code

MF005

5

159497

5

3/18/2018

D4732-23 Manufactured No

100 Each 5.0000 1

D4732-23

Label

**

DAS

6

9-89

Location

Loc Qty

Loc Code

MF005

5

123211

5

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER : ☐							
Misidentified ☐	Past Due ☐								

Picklist Print

Page 4

Wednesday, July 12, 2017 11:31:02 AM

Work Order ID: 164046

164046

Parent Item: D4634-145

D4634-145

Parent Item Name: Aft, Center Ceiling Replacement Panel Assembly

Start Date: 7/13/2017

Required Date: 7/14/2017

Start Qty: 3.00

Required Qty: 3.00

D4732-27

Manufactured No

100

Each

5.0000

1

3

D4732-27

Label

**

DAS

6

9-80

Location

Loc Qty

Loc Code

MF005

5

123213

5

3

MPNY-750S-9-C

Purchased

No

100

Each

644.0000

9

27

MPNY-750S-9-C

Mounting Pad

**

DAS

6

9-80

Location

Loc Qty

Loc Code

ST569

644

M130423

644

9 27

Wednesday, July 12, 2017 11:31:02 AM

Shop Packet Print

Page 4

DQA: _____ Date: _____





WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition			
				Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : ☐					

ITEM	QTY	P/N	DESCRIPTION
1	X	D4634-145	AFT, CENTER CEILING REPLACEMENT PANEL ASSY
2	1	D4634-5	AFT, CENTER CEILING PANEL
3	1	D4636-5	BRACKET
4	1	D4647-1	DOUBLER
5	6	D4664-5	SPACER
6	1	D4712-1	BRACKET
7	1	D4732-17	LABEL
8	1	D4732-23	LABEL
9	1	D4732-27	LABEL
10	1	D5021-5	FOAM, CENTER PANEL, AFT
11	9	MPNY-750S-9-C	MOUNTING PAD
12	4	MS20426AD3-(4)	RIVET, SOLID, CSK
13	2	MS20426AD4-(6)	RIVET, SOLID, CSK
14	2	MS21059L08	NUT PLATE

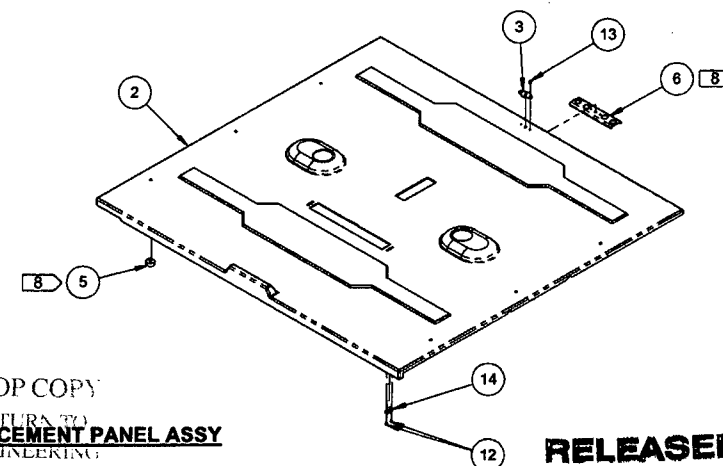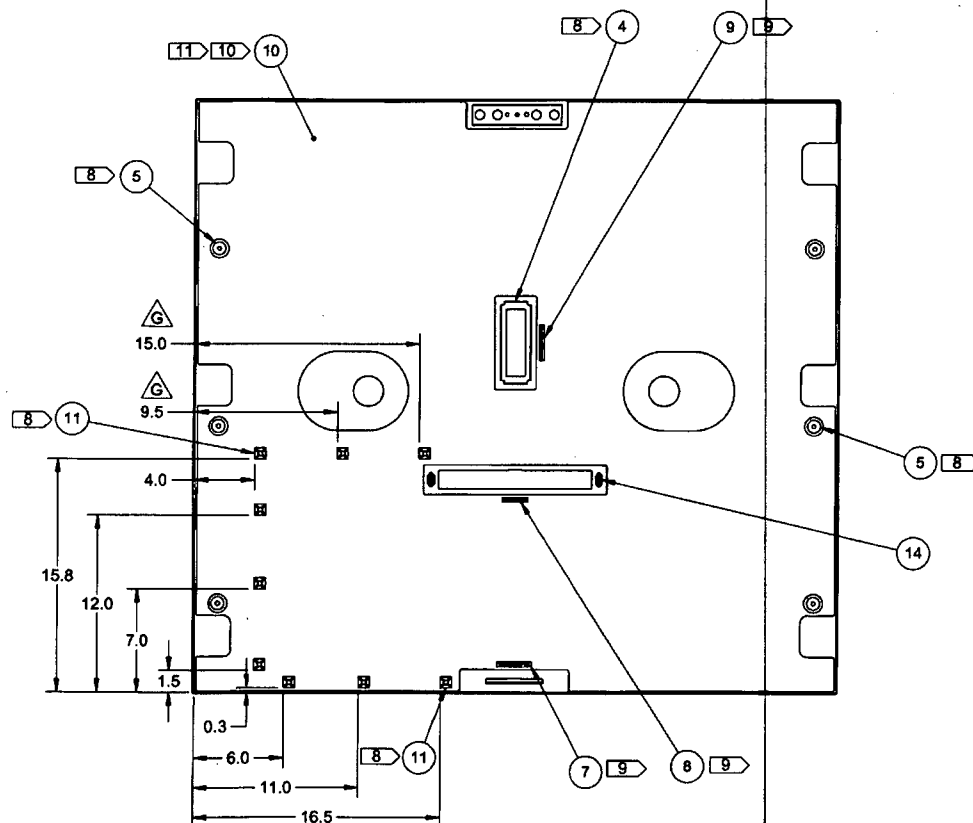

D4634-145 AFT, CENTER CEILING REPLACEMENT PANEL ASSY

NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: N/A
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: N/A
- 7) WEIGHT: N/A
- 8) APPLY A BEAD (0.20 TO 0.30 WIDE) OF DEVCON PLASTIC WELDER II (0.25 INSIDE OF BOTH EDGES OF PART) TO BOND D4647-1 & MPNY-750S-9C. WAIT FOR 2 TO 4 HOURS FOR FUNCTIONAL CURE.
LOCATE D4647-1 IN LINE WITH RECTANGULAR OPENING
- 9) LOCATE LABELS AS SHOWN, SEAL LABELS USING 3950 EDGE SEALER OVER LABEL TOP SURFACE
- 10) APPLY AN EVEN COAT OF 3M SCOTCH WELD 1300L CONTACT ADHESIVE TO BOND D5021-5 FOAM CORE TO INSIDE OF PANEL
- 11) CENTER D5021-5 FOAM ON D4634-5

SHOP COPY

RETURN TO
UNCONTROLLED C.
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 164045

JUL 12 2017

APPROVED

DESIGN	RF	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	RF		
CHECKED	AK	DRAWING NO.	REV. G
MFG. APPR.	DL	D4634	SHEET 9 OF 17
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	CENTER CEILING PANELS	NTS
DATE	14.11.28	COPYRIGHT © 2012 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL, AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

RELEASED
2015 JAN 26
